

WEBSITE READINESS AND SEO AUDIT


Ryan Jewels Launch Audit

Current completion, remaining UI and features, live deployment blockers, SEO readiness, launch plan, and realistic growth timeline.

Audit date	August 7, 2026
Project	Ryan Jewels Ecommerce Website
Live domain reviewed	ryansjewelers.litekart.in
Overall launch readiness	Approximately 58%
Recommended status	Not ready for public marketing yet

Where the website stands today

Bottom line: the Ryan visual layer is progressing well, but the live domain is still loading a generic Test/default storefront. Deployment configuration, sitemap, payment verification, production OTP, broken routes, and SEO metadata must be fixed before launch.

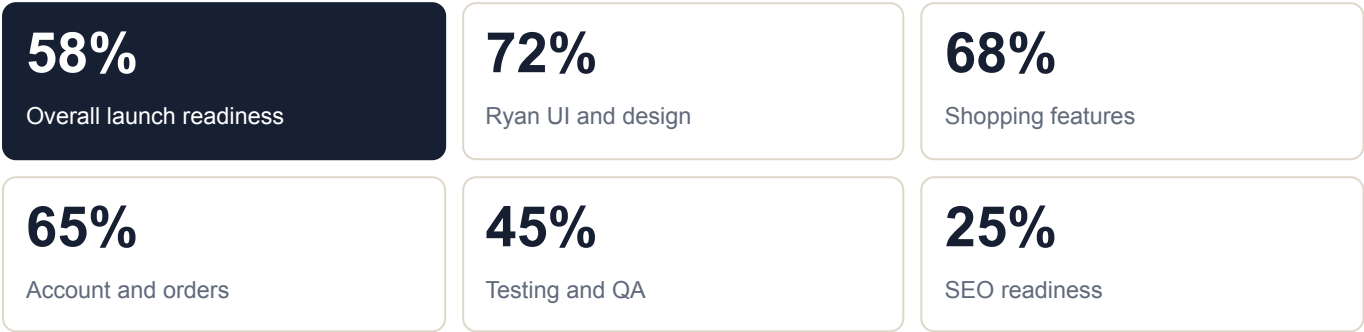

Area	Current condition	Assessment
Ryan theme	Homepage, products, cart, checkout shipping, account dashboard, tracking and order details are substantially themed.	Good progress
Live deployment	Live domain renders Test/default storefront instead of Ryan configuration.	Critical blocker
Checkout and payments	Checkout flow exists; production gateway, webhook and failure recovery are not fully verified.	Needs E2E QA
SEO	Local homepage metadata is useful, but live metadata, sitemap and structured data are broken or generic.	Not launch ready
Code quality	Production build passes, focused Ryan tests pass, but the full code check has extensive pre-existing errors.	Cleanup required

Verified positive signals

- Production build completes successfully, with warnings.
- Focused Ryan admin-menu and product-filter tests pass: 3 tests.
- Local checkout email OTP diagnostic passes.
- Recent tracking number display/copy and account profile work is functioning locally.

Completed UI and remaining pages

Ryan-themed areas completed or advanced

- Navigation, search interface, mega menu and footer
- Homepage sections
- Product listing and product detail
- Cart and checkout shipping
- Account dashboard and order history
- Track-order input and result pages
- Order details, profile and delete account

Pages still needing Ryan design

- Payment, payment success and payment failed
- Wishlist and address-book list/add/edit
- Login, signup, forgot-password and real OTP screens
- Category landing pages
- About, Contact, complete FAQ and Blog
- Privacy, Terms, Shipping, Returns and warranty policies
- 404, error and empty states

Missing or incomplete feature work

Feature	Current behavior	Required action
Product compare	Only localStorage behavior exists.	Add a real compare page.
Product customization	Modal component exists but is not wired into the product flow.	Connect the modal and persist selections.
Notification toggle	UI interaction only.	Persist preference through backend.
Save Card / Gift option	Currently toast-only.	Implement or hide until supported.
Dashboard stats	Development fake data is used for preview.	Connect real messages, orders and coupons.
Buy Again	Uses an incorrect product route in current code.	Change to the canonical product URL.
Verify OTP page	Fake success toast and redirect; no actual verification service call.	Wire real verification and resend flow.
Invoice	Can fall back to browser print when backend invoice is unavailable.	Verify downloadable production invoice.
Order tracking	Tracking number depends on backend fulfillment assignment.	Verify assignment and carrier updates end to end.

Dedicated Ryan pages are also missing for: Customize, Gift Card, Search Results, Compare, Saved Cards, Messages and Coupons.

Critical blockers found

Priority	Finding	Impact
P0	Live domain shows store title "Test" and the default theme instead of Ryan.	Customers do not see the intended storefront.
P0	Live /sitemap.xml returns HTTP 500: Store not found.	Search discovery and crawling are blocked.
P0	Live title and description are generic, OG title is Test, and OG image is blank.	Poor search and social-sharing appearance.
P0	JSON-LD URLs can become https://https://... because the code prefixes an already complete origin.	Invalid structured data.
P0	Latest Profile, Tracking, Order Details and Delete Account work is uncommitted and unpushed.	Local work cannot appear live.
P0	Vercel config contains old demo/API host values that do not match the Ryan environment.	Likely source of live store/theme mismatch.
P1	/categories/lab-grown-diamond is a local and live 404.	Broken primary navigation and SEO landing page.
P1	Ryan assets total about 20 MB across 321 files; several PNGs are 1-2.3 MB.	Slower mobile performance.

Build and code-health evidence

- **Build:** passes with warnings.
- **Focused tests:** pass.
- **Full code check:** 721 errors and 156 warnings across 275 files.
- **Diff hygiene:** trailing whitespace/line-ending issues remain in order-details and tracking files.
- **Automation:** no CI workflow found.
- **Analytics:** a Google Analytics component exists, but ecommerce event instrumentation was not found and the store GTM ID is empty.

Live performance snapshot

Direct unthrottled browser checks showed approximately 127-128 resource requests, about 718 KB transferred, and DOMContentLoaded around 1.95-2.75 seconds. Console output included a homepage Not Found error, a DNS resource failure, and a 404. These are useful diagnostics, not a substitute for post-deployment mobile Core Web Vitals testing.

SEO readiness: approximately 25%

SEO work should begin only after the correct Ryan store is deployed. At present, the live domain's identity, sitemap and structured data are unreliable, so content growth will not compound properly.

SEO area	Finding	Next action
Crawlability	Robots file responds, but its referenced sitemap path and root sitemap behavior are inconsistent.	Generate a valid store-specific sitemap and submit it to Search Console.
Metadata	Local Ryan homepage is better; live uses Test/generic metadata. Products page retains Arialshop women's-fashion defaults.	Set unique Ryan titles and descriptions for every template.
Structured data	Malformed absolute URLs and inconsistent product branding are possible.	Fix URL construction; validate Organization, WebSite, Breadcrumb and Product schema.
Indexing	No meaningful indexed footprint was found for the live domain.	Verify ownership, submit sitemap and request indexing after deployment.
Content	Important category, education and policy pages are missing.	Create unique commercial and informational landing pages.
Performance	Large image assets and many requests may hurt mobile metrics.	Convert/compress images, lazy-load and retest Core Web Vitals.

Recommended SEO content structure

Commercial pages

- Lab-grown diamond engagement rings
- Diamond shapes and carat ranges
- Wedding rings and anniversary jewelry
- Metal, setting and style collections
- Custom ring design and appointments

Helpful content

- Diamond 4Cs and certification guides
- Ring size and setting guides
- Lab-grown vs natural diamond education
- Care, warranty, shipping and returns
- Buying guides, FAQs and customer stories

Reference standards

- [Google: Build and submit a sitemap](#)
- [Google: Ecommerce structured data](#)
- [Google: Request crawling and indexing](#)

Recommended launch roadmap

P0 Must finish before launch

1. Correct live domain/store/theme environment mapping and Vercel values.
2. Commit, merge and push the latest Ryan account, tracking and order-details work.
3. Repair sitemap, metadata, canonical URLs and structured data.
4. Verify payment gateway, webhook, success/failure states and refunds end to end.
5. Configure production SMTP and OTP secrets, then verify signup/login/checkout OTP.
6. Remove fake checkout testimonials, counts and development-only account data.
7. Fix broken routes, especially category, Buy Again and footer cart URLs.
8. Complete mobile, accessibility and browser QA for the purchase journey.

P1 Complete immediately after core launch blockers

- Ryan payment and result pages
- Wishlist
- Address book
- Authentication screens
- Customize flow
- Search results
- Category landing pages
- Legal and policy pages
- 404/error states
- Invoice download
- Analytics ecommerce events
- Image optimization

P2 High-value growth features

Conversion

- Ring builder and customization
- Product comparison
- IGI certificate viewer
- Ring-size guide
- Financing/payment estimator
- Virtual appointment booking

Retention

- Stock and price alerts
- Shareable wishlist
- Verified photo/video reviews
- Recently viewed products
- Saved cart
- Loyalty and referral program

Estimated delivery

Minimum safe launch: about 1-2 focused developer weeks. **Full Ryan design consistency:** about 3-5 weeks, assuming timely payment, SMTP, backend and deployment access.

Realistic SEO and business timeline

Important: if the current Test/default live configuration remains, meaningful SEO growth is unlikely. The timeline below starts after a correct Ryan deployment, working sitemap, clean metadata and useful original content.

Week 1-2 - Launch foundation

Deploy the correct Ryan store, remove blockers, configure Search Console and analytics, submit sitemap, and verify critical transactions.

Week 2-6 - Brand discovery

Brand pages and key products can begin appearing in search if crawl signals are clean.

Month 2-3 - Long-tail signals

Specific product, style, shape, carat and educational queries can start gaining impressions.

Month 3-6 - Consistent non-brand traffic

Quality category pages, helpful guides, reviews and links may build stable organic visits.

Month 6-12 - Meaningful SEO-assisted sales

A consistent publishing, authority and conversion program can produce measurable revenue.

12+ months - Broader competitive terms

High-volume jewelry and diamond keywords generally require sustained authority, links, inventory depth and excellent customer signals.

Launch acceptance checklist

- Ryan theme visible on live domain
- No Test/default branding
- Valid sitemap returns 200
- Canonical and schema URLs valid
- Checkout payment succeeds
- Payment failure is recoverable
- OTP works in production
- Order and tracking records update
- Invoice downloads correctly
- All primary navigation routes work
- Fake data removed
- Mobile purchase flow tested
- Analytics records ecommerce events
- Search Console configured

This completion estimate is an engineering and launch-readiness assessment based on the current repository and live-domain checks. It is not a promise of search rankings or revenue; growth also depends on inventory, pricing, content quality, authority, customer trust and marketing consistency.
